

MISTRY ASSOCIATES

CONSULTING CIVIL ENGINEER

ARCHITECTURAL & STRUCTURAL DESIGNER

NIKUNJ I. MISTRY

(B.E. CIVIL, MIE, CHARTERED. ENGG.)

(FIV, APPROVED VALUER)

Branch : 203 , Riddhi Siddhi Complex , Near Indian Bank , Telephone Exchange Road, Vapi -396195.
Dist.-Valsad. Contact No. 09825512075 / 09825512975

Ref. No.: BC/BBEL/25-26/05

Date 02-09-2025

To,
The Director,
M/s.BBELL Industry LLP
Plot No.DP 119 , GIDC Saykha, Vagra
Dist- Bharuch , Gujarat - 392140

Dear Sir,

Sub:- Contractors' R.A. Bill 05 Invoice No.G042/2025-26 Dtd. 02-09-2025 for the Construction of Road work carried out at Plot No.DP-119, GIDC Saykha , Vagra , Dis. Bharuch, Gujarat 392140

This is with reference to the subject referred above. The contractor DNS Innovation,Vapi-396191 has submitted their R.A.Bill 05 Invoice No. G042/2025-26 Dtd. 02-09-2025 for the Construction of Road work carried out at Plot No.DP-119, GIDC Saykha , Vagra , Dis. Bharuch, Gujarat 392140

We have scrutinised the same at site and its comes as under.

Bill No.	Date	Bill Amount	Certified Amount
G042/25-26	02/09/25	Rs.11,30,429.45	Rs. 1130429.45
Add :CGST @ 9% of	Rs. 1130429.45		Rs. 101738.65
Add :SGST @ 9% of	Rs. 1130429.45		Rs. 101738.65
Less Retention 5%	Rs. 1130429.45		Rs. -56521.47
Amount with Tax			Rs. 1277385.28
TOTAL PAYABLE AMOUNT			Rs. 1277385.28
Say			Rs. 1277385.00


Hence Wehere by certify the same amount of **Rs.12,77,385.00** only for the payment to the contractor.

Please deduct any PAYMENT MADE or MATERIAL SUPPLIED to them against this job beyond our knowledge and pay them accordingly. Please deduct T.D.S. if required.

Thanking You,

For Mistry Associates,

Prop.



HO : Anand Bhuvan , M.G Road, Bilimora - 396 321 . Dist.-Navsari. Gujarat
E Mail: - mistry_associates@yahoo.co.in / er.nikunjmistry@gmail.com

Tax Invoice

e-Invoice

IRN : 12f825cb078ce00a767cf5a9b41bb172391d6804596b6c-
bc64686f3f1fc523c9

Ack No. : 162521840955130

Ack Date : 2-Sep-25



DNS INNOVATION
FIRST FLOOR, OFFICE NO 104 105, HEENA AVENUE,
NEAR HEENA ARCADE GIDC CROSS ROAD
Vapi, DIST: Valsad
GSTIN/UIN: 24AAOFD8504E1ZK
State Name : Gujarat, Code : 24
Buyer (Bill to)

BBELL INDUSTRY LLP
PLOT NO DP-119,GIDC SAYAKHA, VAGRA
DIST. - BHARUCH,GUJARAT
392140
GSTIN/UIN : 24AAPFK0441G1ZK
PAN/IT No : AAPFK0441G
State Name : Gujarat, Code : 24

Invoice No.
G042/2025-26
Delivery Note

Buyer's Order No.

Dispatch Doc No.

Dispatched through

Terms of Delivery

Dated
2-Sep-25
Mode/Terms of Payment

Dated

Delivery Note Date	
--------------------	--

Destination

SI No	Description of Services	HSN/SAC	Quantity	Rate	per	Amount
1	WORK DONE AS PER ATTACHED SHEET 1 <i>RA BILL NO.05</i>	995425				11,30,429.45
	C GST					1,01,738.65
	S GST					1,01,738.65
	Less : RETENTION - BBELL INDUSTRY LLP					(-)56,521.00

continued to page number 2

This is a Computer Generated Invoice



Tax Invoice(Page 2)

DNS INNOVATION

FIRST FLOOR, OFFICE NO 104 105, HEENA AVENUE,
NEAR HEENA ARCADE GIDC CROSS ROAD
Vapi, DIST: Valsad
GSTIN/UIN: 24AAOFD8504E1ZK
State Name : Gujarat, Code : 24
Buyer (Bill to)

BBELL INDUSTRY LLP

PLOT NO DP-119, GIDC SAYAKHA, VAGRA
DIST - BHARUCH, GUJARAT
392140
GSTIN/UIN : 24AAPFK0441G1ZK
PAN/IT No : AAPFK0441G
State Name : Gujarat, Code : 24

Invoice No.

G042/2025-26

Delivery Note

Dated

2-Sep-25

Mode/Terms of Payment

Buyer's Order No.

Dated

Dispatch Doc No.

Delivery Note Date

Dispatched through

Destination

Terms of Delivery

SI No	Description of Services	HSN/SAC	Quantity	Rate	per	Amount
	R/OOF					0.25
Total						₹ 12,77,386.00

Amount Chargeable (in words)

E. & O.E

INR Twelve Lakh Seventy Seven Thousand Three Hundred Eighty Six Only

HSN/SAC	Taxable Value	Rate	CGST Amount	SGST/UTGST Rate	Amount	Total Tax Amount
995425	11,30,429.45	9%	1,01,738.65	9%	1,01,738.65	2,03,477.30
Total	11,30,429.45		1,01,738.65		1,01,738.65	2,03,477.30

Tax Amount (in words) : **INR Two Lakh Three Thousand Four Hundred Seventy Seven and Thirty paise Only**

Remarks:

WORK- ROAD WORK

Declaration

We declare that this invoice shows the actual price of the goods described and that all particulars are true and correct.



for DNS INNOVATION

ABatl
Authorised Signatory

This is a Computer Generated Invoice

To,

Date :- 01/08/2025

B BELL IND. LLP


Saykha Industrial Estate.

Dis. Bharuch ,

Gujarat.

ABSTRACT SHEET					
ROAD WORK					
RA BIL NO.05					
Sr. No.	Service Description	Quantity	Unit	Rate	Amount
5.1	Cutting, bending ,placing in proper position the TMT Steel (FE500) reinforcements in R.C.C.				
a	Ground Floor	2280.18	Kg.	✓ 72.00	✓ 1,64,172.80
11.17	Providing and laying Plain Cement Concrete 1:1½:3 viz. M - 20 of 150mm. average thickness for Trimix Concrete Flooring, using				
a	Ground floor	✓ 419.22	Sq.Mt.	✓ 1,111.00	✓ 4,65,753.42
11.18	Extra over Item 11.17 for applying approved make Floor Hardner (5 Kg/Sq.mt) on Concrete Floor & finishing of the floor using Power Trowel etc.				
a	Ground floor				
a	Mcon - non metallic dry shake floor hardener	✓ 419.22	Sq.Mt.	✓ 100.00	✓ 41,922.00
11.25	Cutting & Filling of Grooves in Trimix floor using				
a	Ground floor				43766.80
1.0	5mm x 10 mm (Trimming from both side)	272.98 198.34	R.Mt.	✓ 220.00	60,055.60
3.0	PLAIN CEMENT CONCRETE				
3.1	Providing and mixing mechanically and laying Plain cement concrete 1:3:6 [M-10 Mix] using 40				
b	In plinth [avg. 100 mm thk.]	✓ 511.662	Sq.Mt.	✓ 560.00	✓ 2,86,530.50
7.12	Grouting pockets, holes, pipes sleeves of any				
b	Non shrink grout including supply of "Conbextra-GP2" or "Sikagrout 214" or approved equivalent	✓ 0.122	Cu.Mt.	✓ 62,000.00	✓ 7,533.00 1071418.94
EX.01	Breaking PCC and disposal	✓ 51.166	Cu.Mt.	2,500.00 2700	1,27,915.40
EX.02	Breaking RCC and disposal	✓ 2.205	Cu.Mt.	5,300.00 4444	11,686.50 9708
EX.03	Electric breaker supply	✓ 8.000	HRS	450.00	✓ 3,600.00
					1130429.45
	TOTAL AMOUNT				11,69,169.22


CHECKED & CERTIFIED FOR THE AMOUNT
Rs. 11,30,429.45/- ONLY
FOR. MISTRY ASSOCIATES




For DnS Innovation


Partner
Partner

MEASUREMENT SHEET

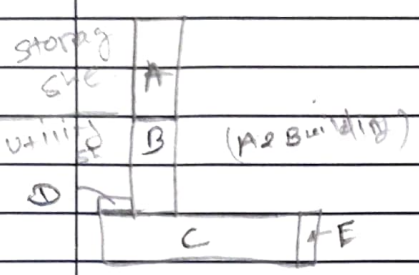Sr.No.	Service Description	Nos	Length	Breadth	Height	Quantity	Unit
5.1	Cutting, bending ,placing in proper position the TMT Steel (FE500) reinforcements in R.C.C.						
a	Ground Floor	1				2280.178	KG
11.17	Providing and laying Plain Cement Concrete 1:1½:3 viz. M - 20 of 150mm. average						
a	Ground floor						
		✓1	✓15.500	✓5.700		✓88.350	
		✓1	✓15.700	✓6.100		✓95.770	
		✓1	✓30.800	✓7.000		✓215.600	
		✓1	✓4.800	✓1.000		✓4.800	
		✓1	✓7.000	✓2.100		✓14.700	
						419.220	Sq.Mt.
11.18	Extra over Item 11.17 for applying approved make Floor Hardner (5 Kg/Sq.mt) on Concrete Floor & finishing of the floor using Power						
a	Ground floor						
a	Mcon - non metallic dry shake floor hardener						
		✓1	✓15.500	✓5.700		✓88.350	
		✓1	✓15.700	✓6.100		✓95.770	
		✓1	✓30.800	✓7.000		✓215.600	
		✓1	✓4.800	✓1.000		✓4.800	
		✓1	✓7.000	✓2.100		✓14.700	
						419.220	Sq.Mt.
11.25	Cutting & Filling of Grooves in Trimix floor using						
a	Ground floor						
1.0	5mm x 10 mm (Trimming from both side)						
	AREA -15.500 X 5.700	✓5	✓5.700			29.450	
		✓2	✓15.500			29.450	15.50
	AREA -15.700 X 6.100	✓5	✓6.100			31.923	
		✓2	✓15.700			31.923	15.70
	AREA -30.800 X 7.000	✓10	✓7.000			71.867	
		✓2	✓30.800			71.867	30.80



No.	Service Description	Nos	Length	Breadth	Height	Quantity	Unit
	AREA -4.800 X 1.000	2	1.000			1.600	
	AREA -7.000 X 2.100	21	2.100			4.900	R.10
						272.980	R.Mt.
						198.94	
3.0	PLAIN CEMENT CONCRETE						
3.1	Providing and mixing mechanically and laying Plain cement concrete 1:3:6 [M-10 Mix] using 40 mm						
b	In plinth [avg. 100 mm thk.]						
		✓1	✓29.540	✓22.040		✓651.062	
	Canteen	-1✓	9.000	✓4.800		✓43.200	
	Lift Pit	✓-1	✓2.100	✓2.400		✓5.040	
		-1	10.600	8.600		-91.160	
						511.662	Sq.Mt.
7.12	Grouting pockets, holes, pipes sleeves of any shape or size, column bases, machine bases etc. including						
b	Non shrink grout including supply of "Conbextra-GP2" or "Sikagrout 214" or approved equivalent						
	Storage Shed Column	12	0.300	0.450	0.075	0.122	
						0.122	Cu.Mt.
EX.01	Breaking PCC and disposal						
	As Building	✓1	✓29.540	✓22.040	✓0.100	✓65.106	
	Canteen	✓-1	✓9.000	✓4.800	✓0.100	✓4.320	
	Lift Pit	✓-1	✓2.100	✓2.400	✓0.100	✓0.504	
		✓-1	✓10.600	✓8.600	✓0.100	✓9.116	
						51.166	Cu.Mt.
EX.02	Breaking RCC and disposal						
		✓1	✓7.000	✓2.100	✓0.150	✓2.205	
						2.205	Cu.Mt.
EX.02	Electric breaker supply						
	Used to make a existing road surface rough	8				8.000	HRS



For Dns Innovation

Atul
Partner

